

Travel & Expenses Sprint Report 10

Sprint Report


Date	22 Aug 2022		
Start	08 Aug 2022	End	22 Aug 2022
Sprint Goal(s)	Go live for Wave 1 (Steerco for Wave 1 - Go Live validation) + Tests readiness validation Finalization of Cognos report / F/u KPI/KVIs / Gather lessons learned from Wave 1 / High-level planning / SOW for Wave 2 / Post Go Live monitoring (Hypercare) NUI - Communication 1: Announcement Concur NUI WW NUI - Modification of e-learning based on feedback		
Sprint report	Sprint 10		
Completed Story Points	55		
Summary	In this sprint, the squad was primarily focused on: <ul style="list-style-type: none"> Go Live for Wave 1 Ensuring Hyper Care post Go-Live Following up on KPIs / KVIs 		
Comments	A full sign-off from the Steerco was required before Go-Live		

TE Sprint 10 ▾




Closed sprint, ended by [Sophie Dubien](#) 08/Aug/22 4:26 PM - 22/Aug/22 3:04 PM [View linked pages](#)

Go live for Wave 1 (Steerco for Wave 1 Go Live validation + tests readiness Validation + finalization of Cognos report) F/u KPI/KVIs Go live for Wave 1 Gather lessons learned from Wave 1 High-level planning / SOW for Wave 2 Post Go Live monitoring NUI - Communication 1: Announcement Concur NUI WW NUI - Modification of e-learning based on feedback

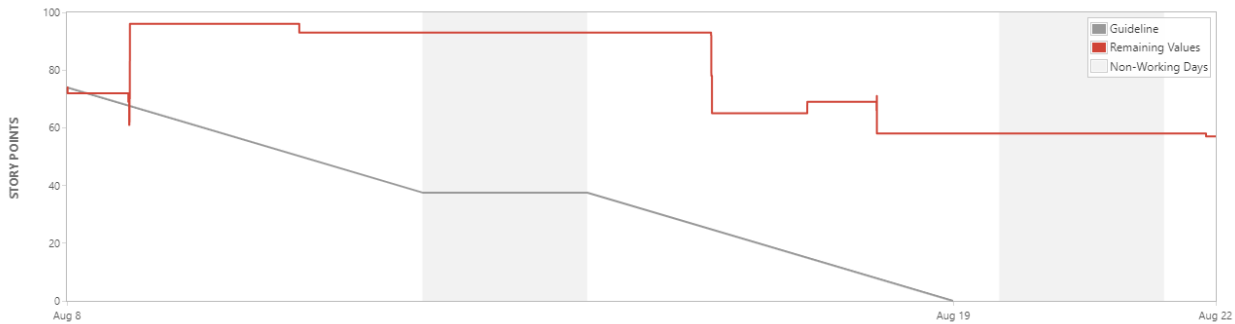





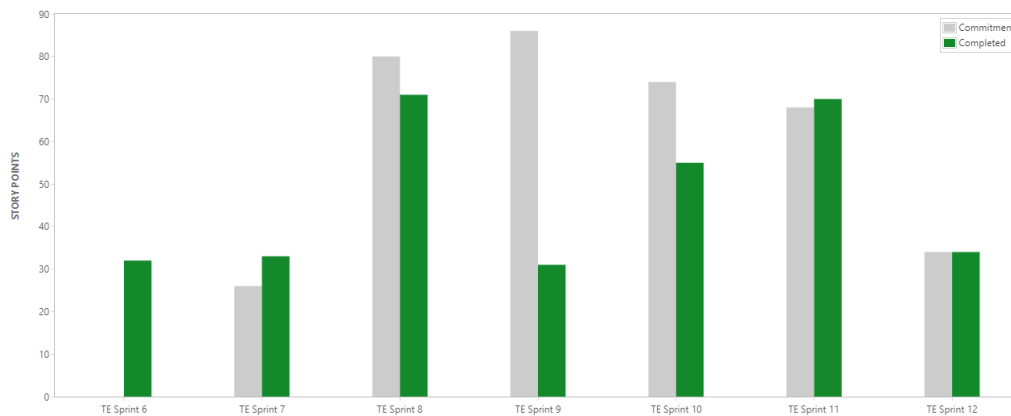

















Velocity Chart

Test View ▾



Completed Issues

[View in Issue Navigator](#)

Key	Summary	Issue Type	Priority	Status	Story Points (48 -- 55)
TE-27	As a developer, I want to have posting scheme for CBCP in order to bring visibility to the full process	 Story	 Highest	DONE	8
TE-234	Create knowledge articles about HSBC in Service One	 Task	 Minor	DONE	13
TE-299	As a PO, I want to have a full sign off in order to go live for Wave 1	 Story	 Minor	DONE	13
TE-309	NUI - Communication 1: Announcement Concur NUI WW	 Task	 Minor	DONE	1
TE-310	NUI - Extract list of employees Solvay + CYTEC	 Task	 Minor	DONE	2
TE-313	NUI - Review and validate current documentation (including translation)	 Task	 Minor	DONE	3
TE-356	Schedule meeting for the lessons learned exercise	 Task	 Minor	DONE	3
TE-358	As a Program Manager, I want timely identification/resolution of issues in Hypercare in order to minimize impact on users	 Story	 Minor	DONE	5
TE-367 *	NUI - Organize Q&A session (Concur NUI) with local connector	 Task	 Minor	DONE	- → 1
TE-394 *	NUI - Communication Key Milestones (Wave 2)	 Task	 Minor	DONE	- → 1
TE-395 *	NUI - Feedback from the local connector on the documentation translated	 Task	 Minor	DONE	- → 5
